

HENTIES BAY INDUSTRIAL SALT PROJECT

Mining Claims 75069–75074 | Industrial Salt | Early Development / Permit & Testwork Stage



A stage-gated Namibian salt project seeking a N\$111.9m total development commitment — N\$6.1m immediately for Phase 1 proof work and N\$105.8m conditionally for Phase 2 scale-up after evidence gates.

Investment thesis: fund the evidence-generating pilot first; release major solar-salt capital only after title, ECC/Dorob/access, product quality, customers, route economics and ownership terms are verified.

01 | INVESTMENT OVERVIEW

PROJECT

MC 75069–75074

Approx. 94 ha | early-development stage

COMMODITY

Industrial salt

Rock salt + refined / value-added products

LOCATION

15 km south of Henties Bay

C34 corridor | Erongo coastal services base

FUNDING FRAME

N\$111.9m staged

N\$6.1m immediate | N\$105.8m conditional Phase 2

INVESTMENT HIGHLIGHT

A staged funding case can close legal, title, access, product-quality, customer and logistics gaps before the larger Phase 2 build. Investor return depends on agreed valuation, equity percentage and capital-release gates — not only on the Phase 1 scoping spend.

EVIDENCE

Tenure / Ownership

Signed application and claim references; certificate/expiry verification outstanding.

Technical Proof Point


ESA/EMP, KML footprint and site evidence; no project assays or resource estimate yet.

Commercial Catalyst

Market analysis supports a modular food/feed-led entry; project-specific LOIs, price formulas, Walvis Bay route terms and offtake remain capital-release gates.

Sources: mining-claim application; ESA/EMP/ECC pack; market analysis; financial model and formal investor-review comments. Status statements reflect evidence currently available.

02 | LOCATION & INFRASTRUCTURE

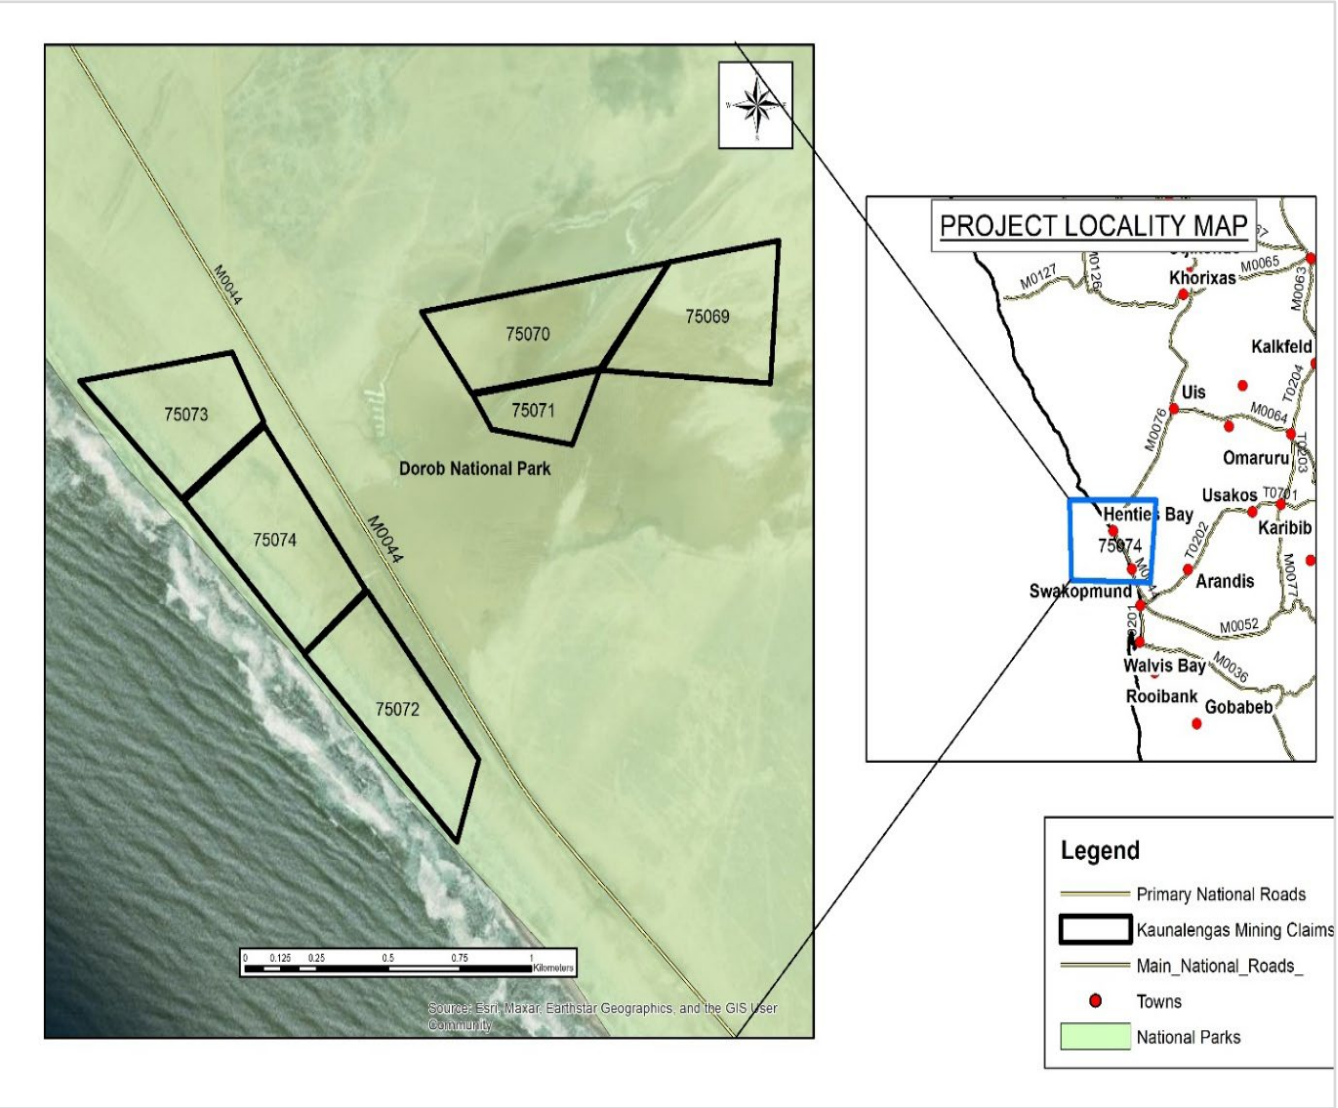

Sources: KML/claim map, ESA/EMP and investor review. Site utilities, pumping route, corridor ownership, port terms and land-access rights are not yet independently verified.

ACCESS

Claims lie beside the C34 coastal corridor, with road access to Henties Bay, Swakopmund and Walvis Bay.

LOGISTICS

Erongo provides mining, engineering, laboratory, port and freight services. Walvis Bay export is a logical route, but haulage, port, warehouse, freight-forwarding and handling quotations remain required.

UTILITIES

No grid, water source or telecom solution is verified. The claim blocks are not contiguous; Phase 1 must define whether brine/water transfer, pumping, pipeline corridors and servitudes are required.

WORKFORCE

Regional operating and contractor skills are available through the Henties Bay–Swakopmund–Walvis Bay corridor.


LAND / COMMUNITY

State land within Dorob National Park. Written park consent, lawful access, inter-claim corridor rights, accessory-work permissions and stakeholder engagement remain conditions precedent.

03 | MINERAL RIGHTS & OWNERSHIP

Henties Bay Industrial Salt Project - Claim Layout

Six mining claims | Official project area: 94.32 ha | Coordinate-based schematic

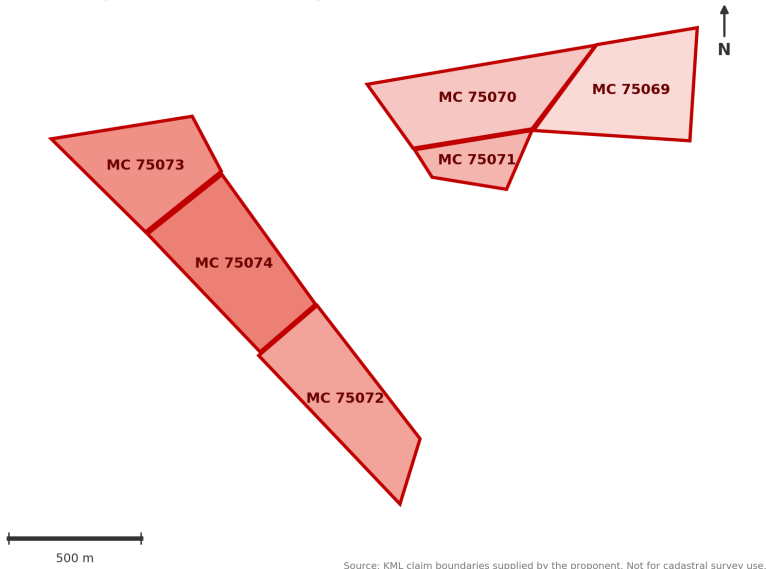

RIGHT / LICENCE MC 75069–75074 referenced across the ESA/EMP and project documents.

APPLICANT / PROPONENT Kaunalenga Kristof Tangeni Avia (natural person). Holder-of-record status requires certificate verification.

STATUS / VALIDITY Pegged 11 Nov 2023; application signed 13 Nov 2023. Registered claim certificates and expiry dates are not in the current pack.

ECC / CONSENTS ECC APP 241118004975; ESA Apr 2025 and EMP May 2025. ECC certificate not evidenced. Dorob consent requested 15 Jul 2025; response not evidenced.

LAND / ACCESS State land within Dorob National Park. Written access/compensation, accessory-works rights and operating permits are not evidenced.

TRANSACTION READINESS Proposed structure: project-level equity/JV or milestone-based funding after tenure, ECC, Dorob and land-access verification.

Application face shown for evidence; it is not a registration certificate.

Sources: signed MC application; ESA/EMP; ECC application documentation; Dorob consent request. Replace the application face with current registered certificates and expiry evidence if available.

04 | GEOLOGY & MINERALISATION

DEPOSIT SETTING	Flat, low-lying coastal saline-pan environment on Namibia’s central Atlantic coast.
HOST MATERIALS	ESA describes saline and gypsiferous soils, evaporite crust and low-permeability substrate.
MINERAL TARGETS	Rock salt / halite, gypsum and brine-derived solar salt; anhydrite is a secondary conceptual target.
CONTROLS	Hyper-arid climate, low rainfall, high evaporation and shallow depressions support an evaporite concept.
DISTRICT CONTEXT	Established salt production and industrial-mineral activity occur along the Erongo coast.
RESOURCE STATUS	No verified thickness, continuity, NaCl grade, brine chemistry, resource estimate or reserve is in the current pack.



Flat saline-pan surface observed in the project area



Salt-bearing crust



Solar-evaporation analogue

INVESTOR INTERPRETATION

The geological case supports targeted testwork—not a resource claim. Field mapping, trenching, representative assays and brine chemistry are the next proof points.

Source: April 2025 ESA and site photographs. Geological descriptions are conceptual/desktop evidence and are not a mineral-resource statement.

05 | TECHNICAL EVIDENCE & PRODUCTION BASIS



Current evidence maturity: concept / environmental baseline. Accredited technical proof is the funded next step.


VERIFIED IN THE CURRENT EVIDENCE PACK	NOT YET VERIFIED / INVESTOR-CRITICAL
• Six-claim footprint and coordinates, with an area reconciliation requirement. • Signed mining-claim application and claim references. • Public notices, site photographs, ESA and EMP. • Coastal saline-pan / evaporite development concept. • Screening market analysis and financial model.	• Registered claim certificates, holder-of-record and expiry. • ECC certificate, written Dorob consent and lawful land access. • NaCl grade, thickness, continuity and brine chemistry. • Resource / reserve, recovery, yield and production mass balance. • Customer sample acceptance, LOIs/offtake and firm vendor / route quotes.

PRODUCTION BASIS	Phase 1 planning basis	Phase 2 planning basis	Commercial proof gate
	15,000 tpa / 1,250 t per month in the screening model. This is a pilot planning assumption, not resource-backed capacity.	233,730 tpa steady-state saleable output in 2031 model. Requires resource, brine, pond, yield and market reconciliation.	At least two buyer-acceptable product grades and two anchor LOIs/offtakes totalling ≥2,500 tpa before commercial commissioning.



Sources: ESA/EMP, KML footprint, financial model and referenced market analysis. No project-specific assays, resource estimate or customer acceptance evidence is in the current pack.

06 | VALUE CREATION PLAN

THREE VERIFIED PROJECT MILESTONES



WHAT THE IMMEDIATE N\$6.1m PROGRAMME UNLOCKS TOWARD THE N\$111.9m STAGED COMMITMENT

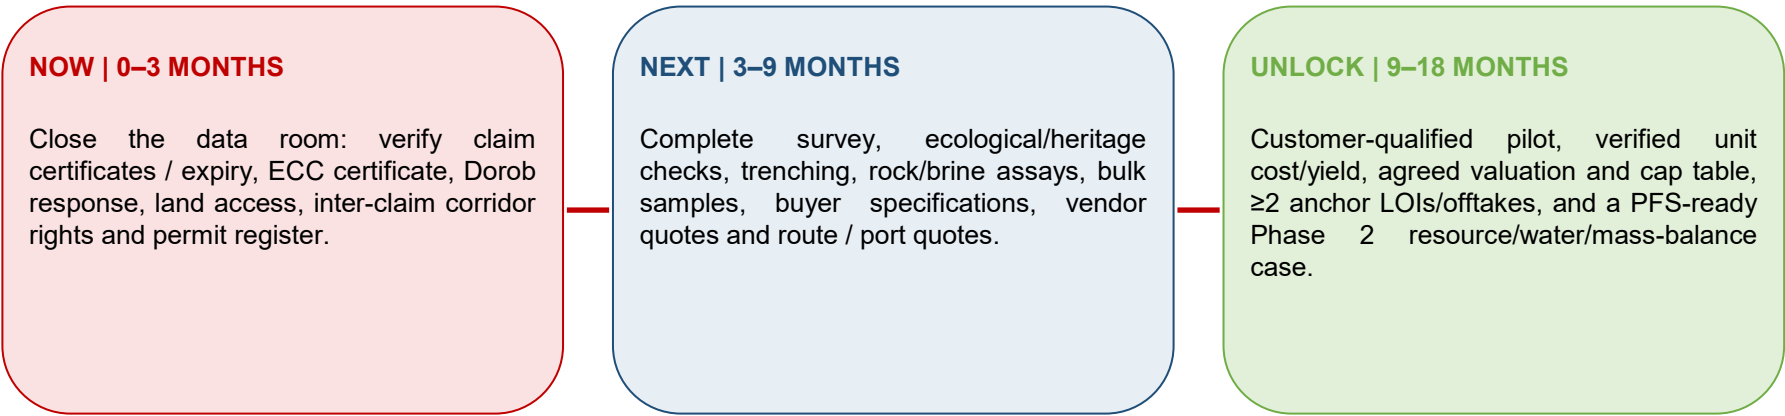

Sources: signed claim application; public notices; ESA/EMP; Dorob consent request; financial model; market-analysis investment gates.

07 | DEVELOPMENT CONCEPT & MARKET



Salt-bearing surface / rock-salt target



Solar evaporation / crystallisation concept



Flat saline-pan operating setting

01 RESOURCE & QUALITY

Survey, mapping, trenching, rock/brine chemistry, representative samples and buyer-defined product specifications.

02 CONTROLLED PILOT

Selective cutting or excavation, drying, crush/screen, contamination control, packing and verified unit-cost measurement.

03 CUSTOMER QUALIFICATION

Accredited COAs, fish/food/feed trials, private-label or specialty samples, repeat orders and anchor LOIs/offtakes.

04 PHASE 2 SCALE-UP

Only after PFS/DFS: brine intake, ponds, harvesting, washery, packaging and regional distribution.

MARKET PATH

PHASE 1 PRIORITIES

- Feed / rock-salt blocks
- Fish / food B2B
- Washed coarse trials
- Specialty / private-label pilots

NOT PHASE 1

- Bulk chemical export
- Mass retail price war

WALVIS GATE
Port, haulage and forwarder quotes + ≥2,500 tpa anchor commitments.

COMMERCIAL GATE

Do not commission commercially until at least two anchor customers commit a combined ≥2,500 tpa, project samples achieve at least two buyer-acceptable product grades, and delivered/FOB pricing is validated.

Source: referenced 2026 market analysis, financial model and investor review. Product specifications, customer acceptance, price formulas, port handling and route economics remain subject to buyer trials and firm quotations.

08 | TEAM & EXECUTION TIMELINE



Kaunalenga Kristof Tangeni Avia

Project Promoter / Execution Lead

- Namibian mining professional with 15+ years of operational and project experience.
- BSc and GDE in Mining Engineering — University of the Witwatersrand.
- MBA in Finance and Sustainability — University of Cumbria.
- Experience in contractor management, cost optimisation, governance, risk and execution.

CURRENT / CONTRACTED CAPABILITY

- Project promoter / mining and execution lead.
- SS Consultants CC — EAP responsible for the ESA/EMP and ECC application support.
- Financial and market workstreams completed at screening level.

APPOINTMENTS REQUIRED BEFORE MOBILISATION

- Mining-title / land-access counsel and document-control lead.
- Geology, brine chemistry, accredited laboratory and resource lead.
- Process / pond / corrosion engineer and equipment specialist.
- Commercial lead for buyer trials, logistics and offtake.

EXECUTION TIMELINE

0–3 MONTHS

Verify title / expiry, ECC, Dorob and land access; appoint specialists; open data room.

3–9 MONTHS

Survey, testwork, buyer specifications, trials, vendor quotes and pilot design.

9–18 MONTHS

Controlled pilot decision, anchor offtake, verified operating basis and Phase 2 PFS package.

Sources: promoter profile in the current deck; ESA/EMP consultant details. Specialist appointments and formal project-SPV governance remain to be completed.

09 | INVESTMENT ASK

N\$111.9m staged

N\$6.1m immediate | N\$105.8m conditional Phase 2 | ≈US\$6.68m total*

Decision requested

Approve an immediate N\$6.1m Phase 1 proof programme and a conditional right to participate in Phase 2 once title, ECC/Dorob/access, quality, customers, route economics and PFS evidence are complete.

Preferred structure

Preferred: project-level SPV / JV with milestone drawdowns, a negotiated pre-money valuation, clear investor equity %, dilution, board rights, reserved matters and anti-dilution protection.

Timing

Immediate draw only after tenure, ECC, Dorob and land-access CPs. Phase 2 capital only after PFS/DFS, customer/offtake and logistics gates.

INDICATIVE CAPITAL BUILD-UP (N\$ MILLION)

Phase 1 equipment / site assets	2.687
EIA / ECC specialist estimate	0.080
Total Phase 1 cash CAPEX	2.767
Funding reserve / working capital	3.333
TOTAL PHASE 1 ASK	6.100
Phase 2 conditional CAPEX	105.800

TOTAL STAGED COMMITMENT: N\$111.900m

FUNDING UNLOCKS

Title/ECC/Dorob/access close-out • accredited testwork • customer trials and anchor LOIs • route/port quotes • valuation/cap table • controlled pilot • Phase 2 PFS package.

INVESTOR TAKEAWAY

Investor return must be linked to an agreed valuation and ownership percentage. The DCF/NPV is a screening output and should not be treated as the transaction price.

* FX per model assumption: N\$16.76/US\$1. Sources: financial model, capital brief and investor review. Estimates are screening/Class 5 and not PFS/DFS capital or valuation opinions.

SCREENING ECONOMICS & CAPITAL RELEASE GATES

SCREENING-MODEL OUTPUTS

BASE NPV N\$486.3m	IRR 62.4%
WACC 13.18%	PHASE 2 CAPEX N\$105.8m

PHASE 2 CAPEX DETAIL + 10% ADVERSE NPV EFFECT

Phase 2 CAPEX: equipment N\$48.5m; facilities/infrastructure N\$43.5m; contingency N\$13.8m = N\$105.8m. 10% adverse case: revenue NPV N\$345.8m (–N\$140.6m); saleable tonnes N\$411.9m (–N\$74.4m); debt rate N\$456.9m; fixed OPEX N\$471.2m.


CAPITAL RELEASE GATES

GATE 1	Registered claim certificates / holder / expiry, annual compliance, lawful land access and written Dorob consent.
GATE 2	ECC certificate and complete public-participation evidence; permit register and document-control reconciliation.
GATE 3	Survey, assays, brine chemistry, bulk samples and at least two buyer-acceptable product grades.
GATE 4	Pilot design, vendor quotes, Phase 2 Class 4/3 estimate, route/port netback, HSE/corrosion controls and verified cost/yield model.
GATE 5	At least two anchor LOIs/offtakes totalling ≥2,500 tpa, agreed valuation/cap table, investment term sheet and controlled mobilisation.

All financial outputs are preliminary screening-model results—not a resource/reserve statement, valuation opinion, ownership offer or final investment decision forecast.

Source: updated operational/financial model and expanded NPV sensitivity. Validate after resource, process, market, permitting and vendor evidence is complete.

INTEGRATED 5 × 5 RISK ASSESSMENT — INHERENT VS RESIDUAL

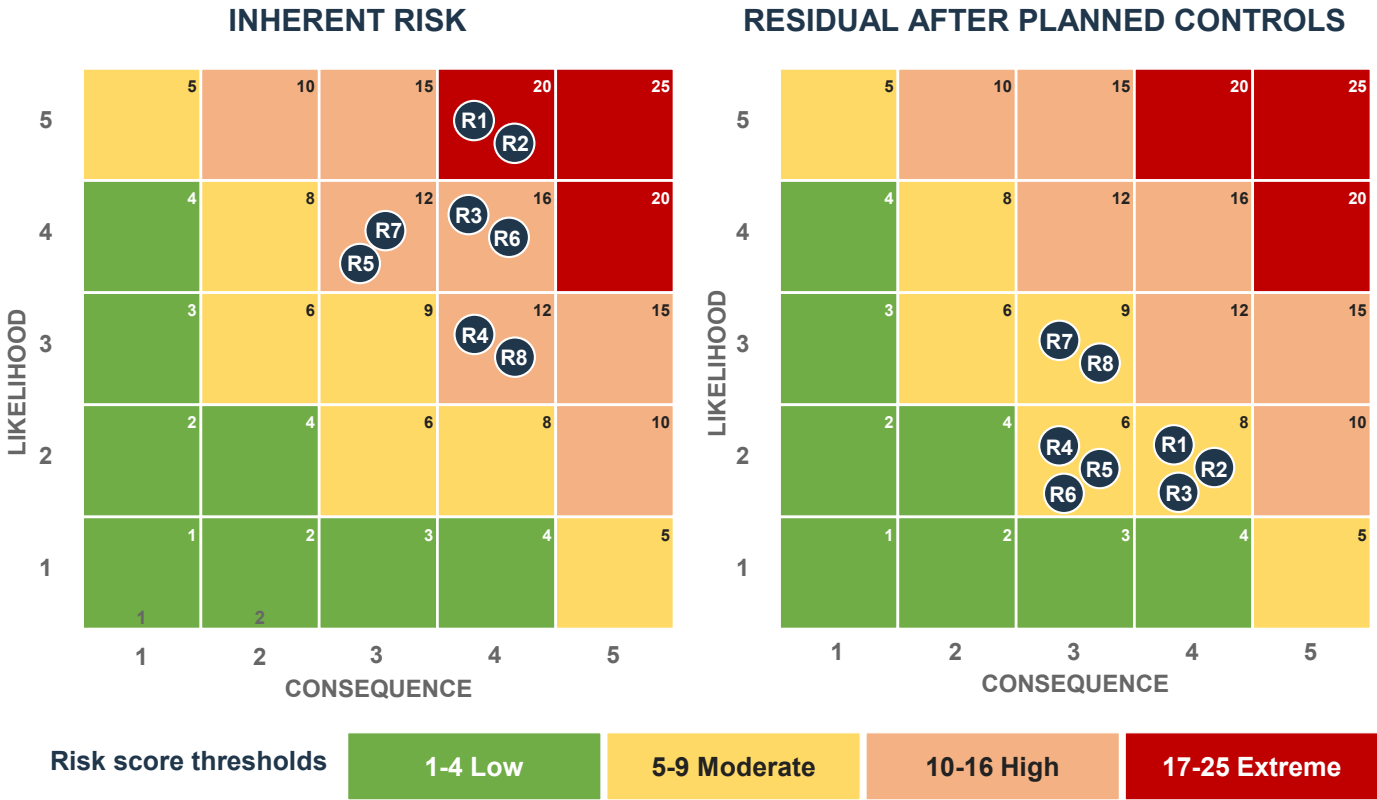


RISK REGISTER	
R1	Title, ECC, Dorob and public-participation completeness
R2	Lichen / vegetation disturbance
R3	Dorob consent, land access, inter-claim corridor and pumping route
R4	Brine / bittern seepage
R5	Habitat / fauna disturbance
R6	Resource, area and product-quality uncertainty
R7	Customer qualification, price, route economics, Walvis Bay logistics and offtake
R8	Funding, Phase 2 CAPEX, dilution, sensitivity and corrosion reliability


CONTROL PRIORITIES

- Do not classify title, ECC, Dorob/access, resource, customer/offtake, valuation or Phase 2 CAPEX risks as green before documentary evidence is obtained.
- Routine HSE, traffic, spill preparedness and site-security risks may move to green after implemented controls, training, audits and monitoring evidence.
- Link assays, customer specs, route quotes, cap table and PFS/DFS evidence to capital-release gates.


RISK CONTROL ARCHITECTURE — SWISS CHEESE, PESTLE AND TOWS

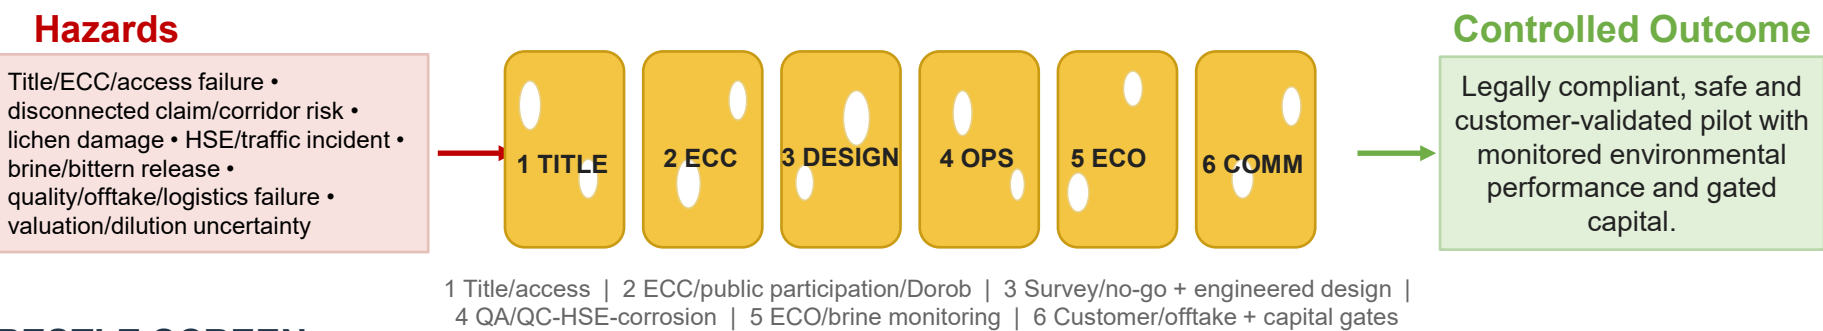

PESTLE SCREEN

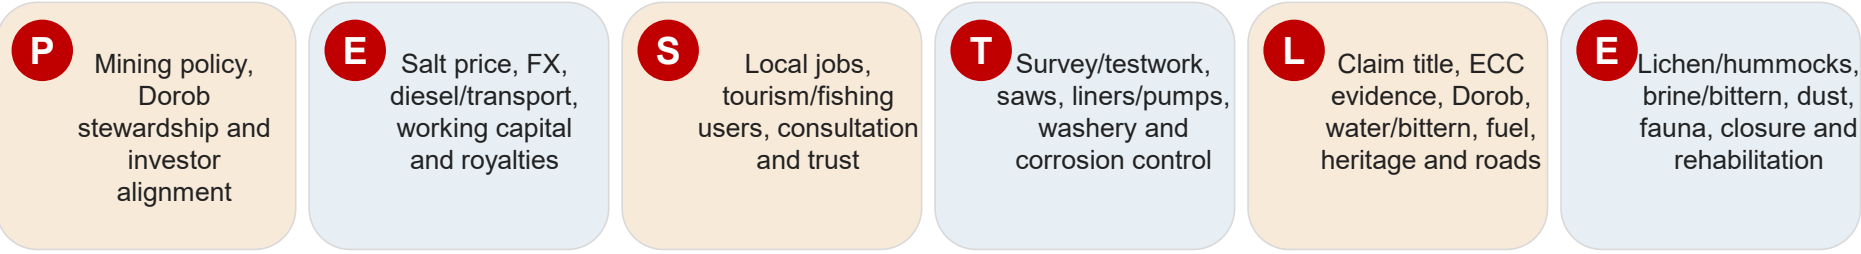

SWOT / TOWS STRATEGIC RESPONSE

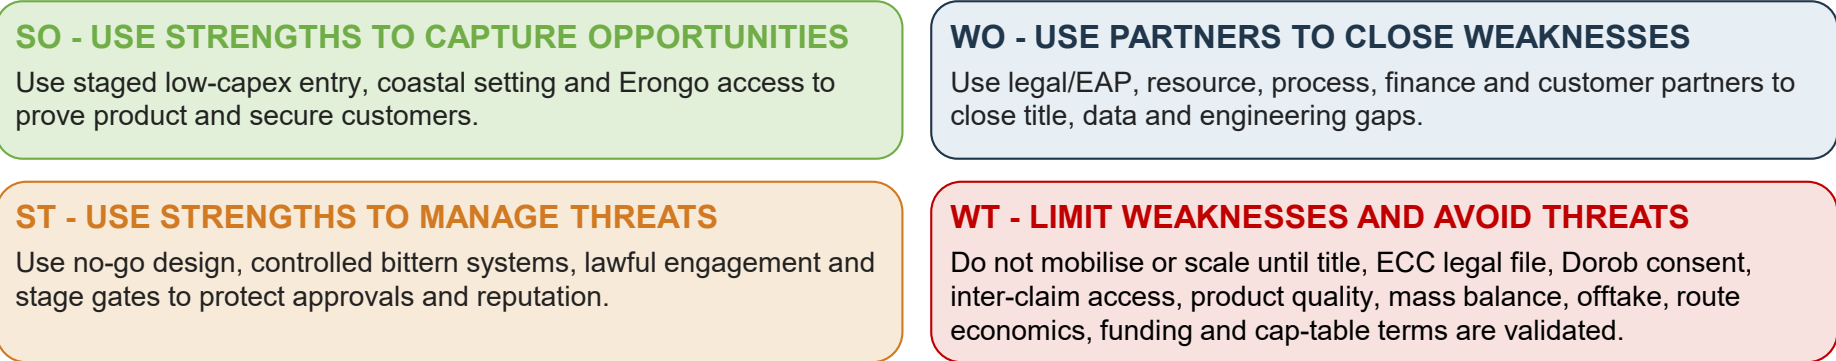

RESPONSIBLE DEVELOPMENT, PERMITTING & STAKEHOLDERS

ENVIRONMENTAL


- Field-verify lichen, coastal hummocks, washes and rock outcrops; establish no-go zones.
- Minimise footprint and use existing/designated access routes within Dorob National Park.
- Engineer ponds and pipelines for seepage control; use one controlled bittern outlet and spill response.
- Monitor brine/bittern, water, dust, fauna, waste and rehabilitation performance.
- Maintain closure security and post-closure monitoring; update the EMP if project scope changes.

SOCIAL & HSE

- Complete lawful public participation, written stakeholder notices, I&AP register, consultation minutes and grievance mechanism.
- Prioritise local employment, procurement and skills transfer in Henties Bay and the Erongo Region.
- Apply road-safety controls, worker induction, PPE, first aid, emergency and heat/fatigue management.
- Protect heritage through pre-work survey and the chance-finds procedure.
- Build customer and community trust through transparent monitoring and performance reporting.

GOVERNANCE & PERMITS

- Verify registered claim certificates, holder-of-record, expiry, annual fees/returns, land access/compensation, inter-claim corridor rights and accessory-works rights.
- Obtain and verify the ECC certificate for APP 241118004975 and written Dorob National Park consent; complete statutory public-participation evidence.
- Secure water/brine/bittern, fuel, heritage/protected-plant, road, pumping route and logistics approvals.
- Reconcile KML/ESA area and inconsistent NPL/EPL, location and report identifiers.
- Conduct monthly ECO inspections, biannual compliance reporting, independent audits and investor governance.



Public notice evidence

**MIME / Mining
Commissioner**

**MEFT / Dorob National
Park**

Water Affairs

**National Heritage
Council**

**Henties Bay
Municipality**

**Communities and
tourism users**

**Customers / offtakers, investors
and technical partners**

FUND THE PROOF PROGRAMME — COMMIT TO SCALE ONLY AFTER EVIDENCE GATES

PARTNERSHIP ASK

- N\$111.9m staged commitment: N\$6.1m immediate Phase 1 proof funding plus N\$105.8m conditional Phase 2 CAPEX after PFS/DFS and commercial gates.
- Preferred: SPV/project-level equity or JV with negotiated valuation, agreed investor %, dilution, board rights, reserved matters and controlled drawdowns.
- Technical partners for title/access, surveying, testwork, resource, process, pumping route, corrosion, pond/washery and PFS development.
- Customer/logistics partners for product specifications, trials, anchor LOIs/offtake, Walvis Bay handling, road haulage and export netback terms.
- Investor reporting to include cap table, evidence register, risk owners, gate status and budget-to-actual tracking.

Investment conclusion: proceed as an evidence-led pilot with protected scale-up optionality, not as an immediate unverified bulk-salt build.

EVIDENCE PACK & FINAL GAPS

AVAILABLE

- Signed claim application and KML/claim maps
- Public notices and site-display evidence
- BID, ESA and EMP
- ECC application reference
- Dorob consent request
- Market analysis and financial model

OUTSTANDING

- Registered claim certificate(s), holder, expiry and annual compliance
- ECC certificate, written Dorob consent and public-participation legal file
- Land access, inter-claim corridor / servitude and pumping route evidence
- Project assays, brine chemistry, resource and production mass balance
- Customer acceptance, price formulas, LOIs/offtake and delivered/FOB netbacks
- Firm equipment, Phase 2 Class 4/3 CAPEX and Walvis Bay logistics quotes

Submit certificates, valuation/cap-table terms, customer evidence and logistics quotes as soon as available; do not replace gaps with unsupported claims.
